

# Sound Transit Light Rail in Redmond

---

August 16, 2022

Vangie Garcia, P.E., PMP

Transportation Planning and Engineering Manager




# Purpose



- Eastlink and Downtown Redmond Link Extension Project Updates

# Where are we?

- 2006 – Environmental review began from Seattle to Downtown Redmond
- 2016 – Overlake construction began
- 2020 – Downtown construction began
-  2023 – Overlake stations open
- 2024 – Downtown extension opens



# Overlake Village Station

View of the Overlake Village Station and Plaza Street from the paperclip ramp






# Redmond Technology Station Garage Reconstruction

All major pours have been completed.

Completion and bus loop opening expected in Q1 2023





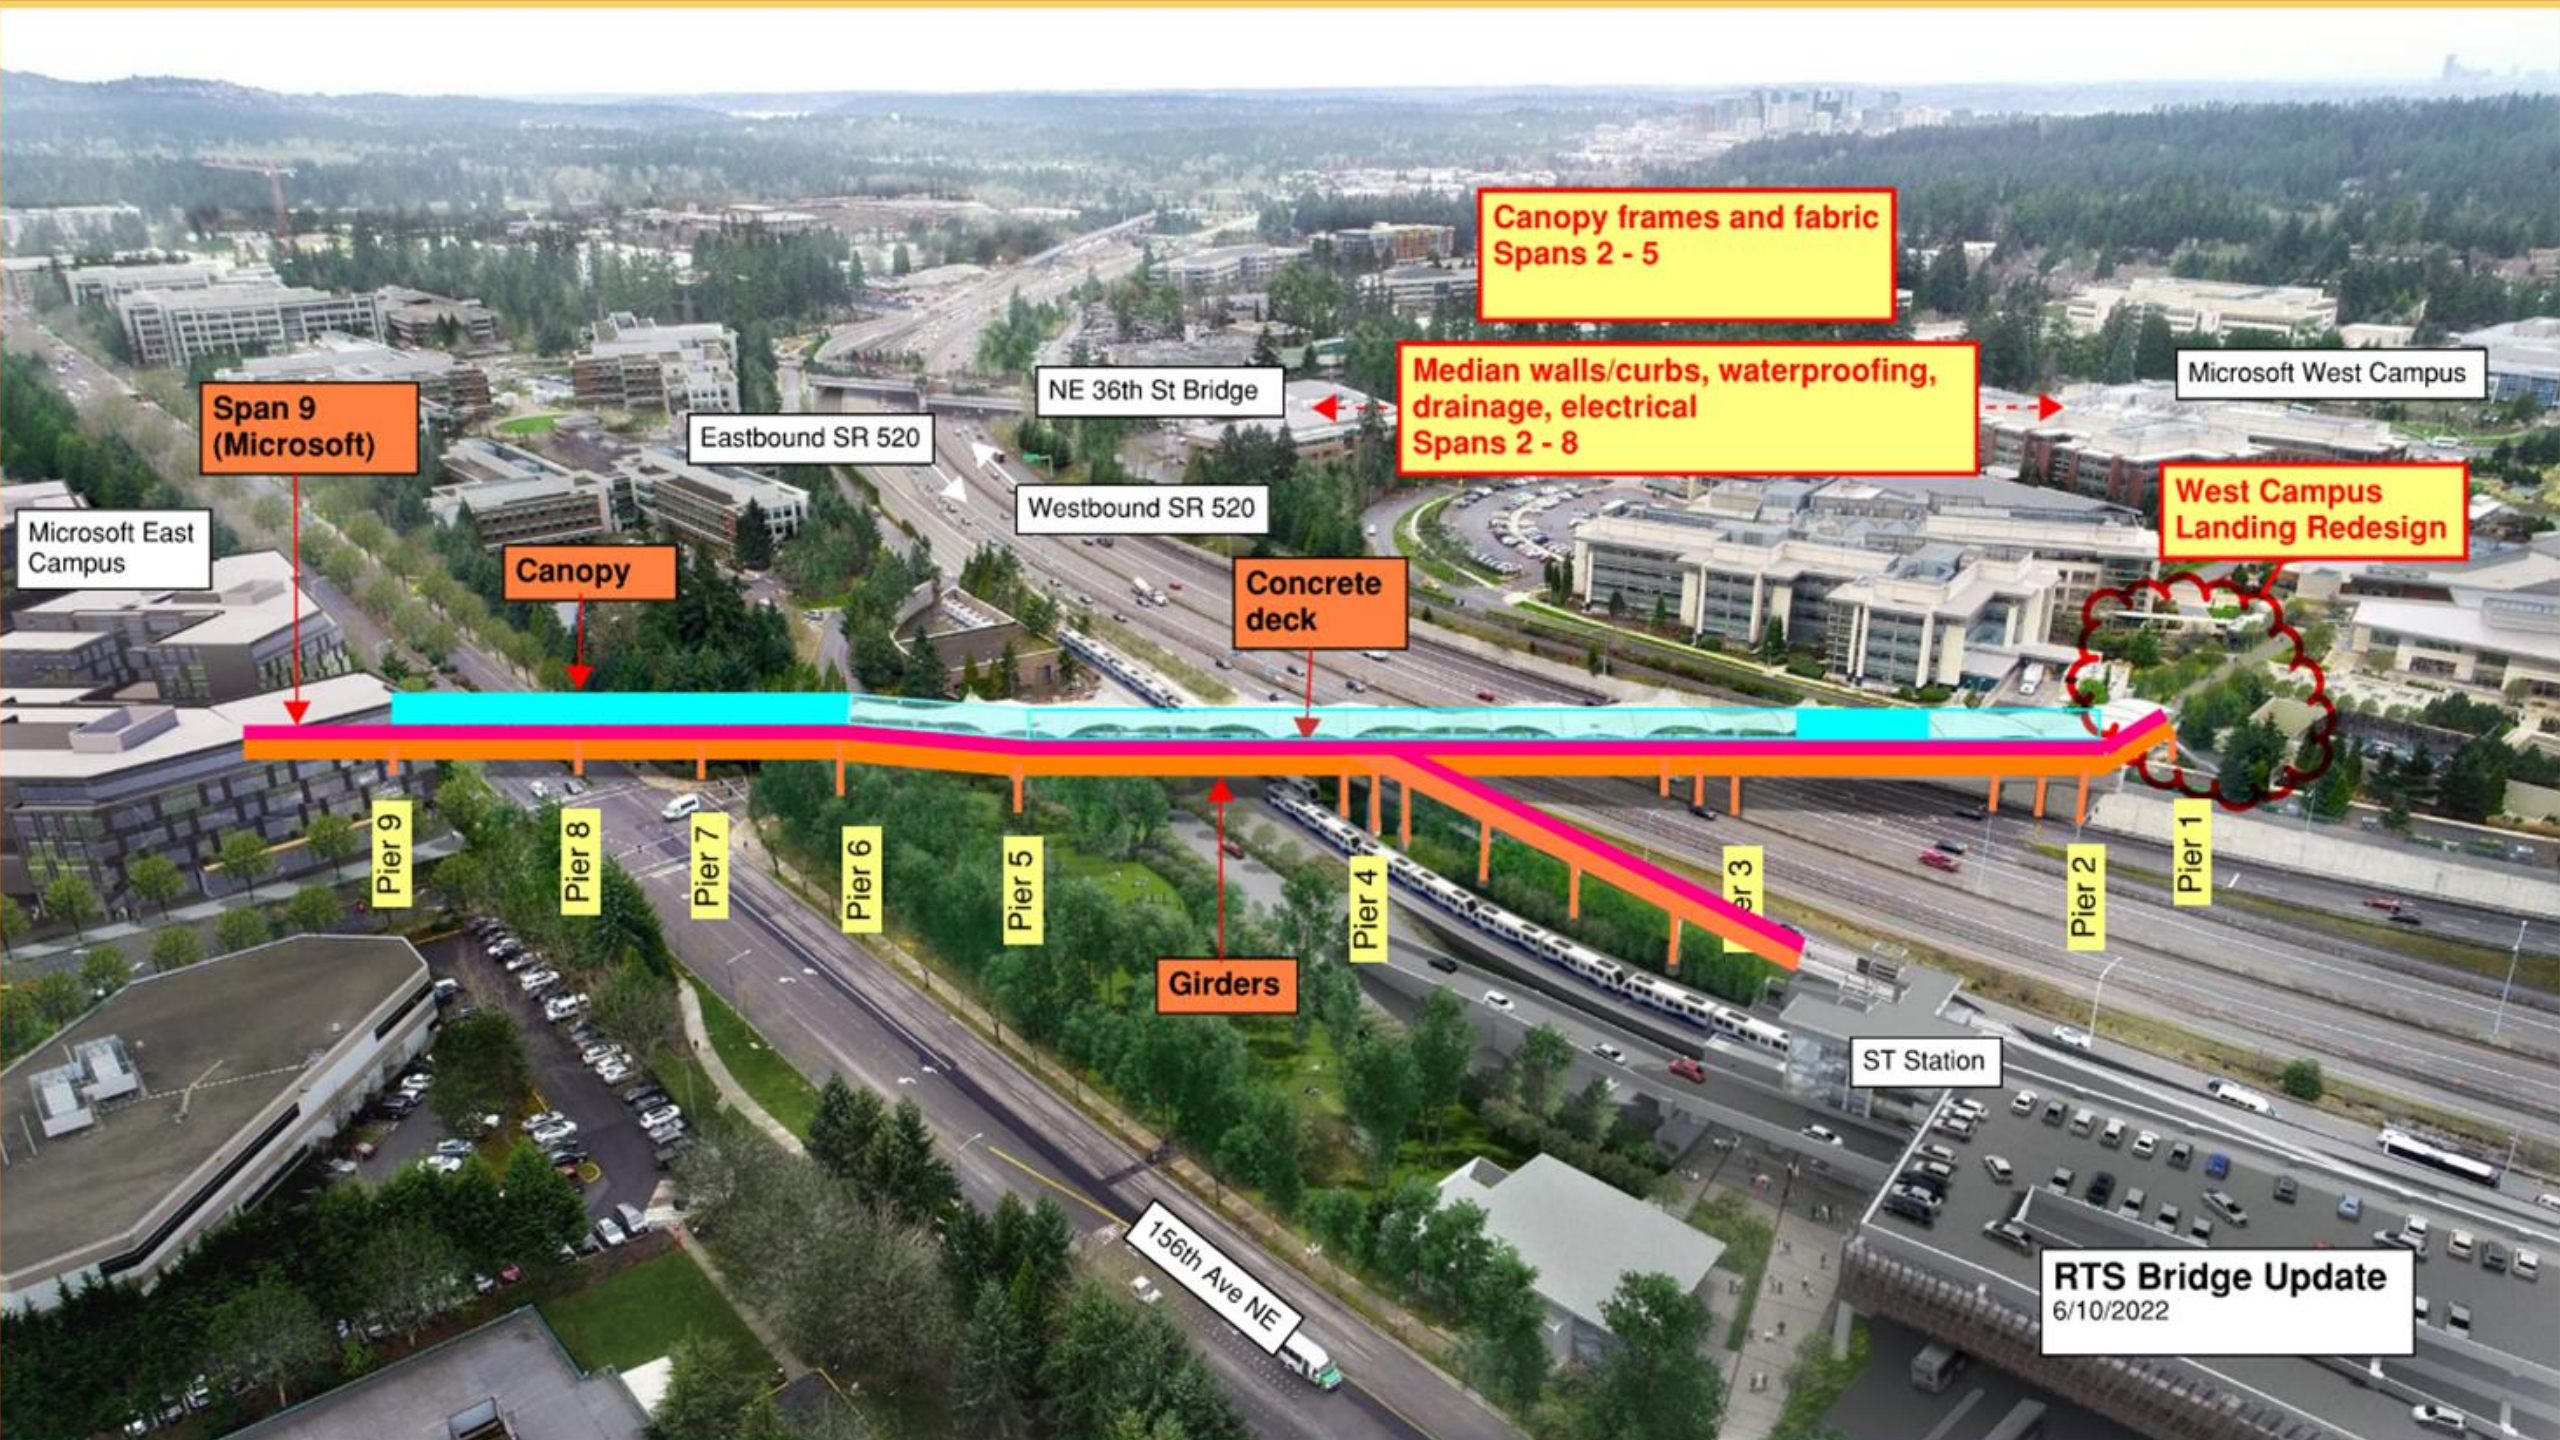

Span 9  
(Microsoft)

Microsoft East  
Campus

Canopy

Eastbound SR 520

NE 36th St Bridge

Westbound SR 520

Concrete  
deck

Median walls/curbs, waterproofing,  
drainage, electrical  
Spans 2 - 8

Canopy frames and fabric  
Spans 2 - 5

Microsoft West Campus

West Campus  
Landing Redesign

Pier 9

Pier 8

Pier 7

Pier 6

Pier 5

Pier 4

Pier 3

Pier 2

Pier 1

Girders

ST Station

156th Ave NE

RTS Bridge Update  
6/10/2022





# Redmond Technology Station Bridge

- Planting in progress
- West stairs ready to install precast concrete treads





# DRLE NE 40th Street Cut and Cover

- Phase 2 – South deck pour was completed on May 27
- Scheduled to open to all lanes of traffic on September 2



# DRLE SR 520 / NE 51st Street

- Opened all lanes of traffic on April 22





# DRLE SR 520 / NE 60th Street

- Soil nail walls are complete
- Contractor forming base and walls for cast in place box
- Scheduled to be open to all lanes of traffic in September



# DRLE SE Redmond/ Marymoor Village

.....

- Parking garage construction now on Level 3
- Final structure will have 1,400 parking stalls





# DRLE SR 520 off-ramp to SR 202

- Off-ramp complete and open to traffic



# DRLE SR 520 on-ramp from SR 202

.....

- Decks have been poured and girders set
- Scheduled to open to traffic in mid to late August







# DRLE

## Bear Creek and into Downtown

- Crews continue to work on pedestrian bridge and walls
- Structure B into Downtown – all girders set and constructing decks





# DRLE Downtown Structure B

- Crews continue to work on end diaphragms and on deck reinforcement



# Thank You

---

Any Questions?

